

Dedham Early Childhood		1					2018												2019	
Activity ID	Activity Name	OD	RD	Early Start	Early Finish	TF	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb			
Dedham Early Childhood		319	182	22-Sep-17 A	21-Dec-18	0											21-Dec-18, Dedham E			
Milestones / Key Events		160	160	07-May-18	21-Dec-18	0											21-Dec-18, Milestones			
3450	Weather Tight - Area C	0	0		07-May-18	9											◆ Weather Tight - Area C			
3660	Weather Tight - Area B	0	0		22-May-18	0											◆ Weather Tight - Area B			
3770	Weather Tight - Area A	0	0		24-May-18	10											◆ Weather Tight - Area A			
6370	Permanent Power " On Line"	0	0		01-Oct-18	19											◆ Permanent Power " On Line"			
3800	Substantial Completion (FNLT (12/21/18))	0	0		21-Dec-18	0											◆ Substantial Completio			
Change Management		42	17	16-Feb-18 A	30-Apr-18	19											30-Apr-18, Change Managment			
MEP/FP Coordination/Revised Ceiling Modifications		42	17	16-Feb-18 A	30-Apr-18	19											30-Apr-18, MEP/FP Coordination/Revised Ceiling Modifications			
D300	Project Team conduct Coordination & Resolve Conflicts	40	2	16-Feb-18 A	09-Apr-18	19											Project Team conduct Coordination & Resolve Conflicts			
D310	Duct & Pipe Fabrication	15	15	10-Apr-18	30-Apr-18	19											Duct & Pipe Fabrication			
Procurement		228	91	22-Sep-17 A	14-Aug-18	53											14-Aug-18, Procurement			
064000 - Architecural Woodwork		93	43	06-Feb-18 A	06-Jun-18	75											06-Jun-18, 064000 - Architecural Woodwork			
360	Rev and Appv - Architecural Woodwork	15	3	06-Feb-18 A	10-Apr-18	75											Rev and Appv - Architecural Woodwork			
370	Fab and Deliver - Architecural Woodwork	40	40	11-Apr-18	06-Jun-18	75											Fab and Deliver - Architecural Woodwork			
066116 - Solid Surfacing Fabrications		101	51	06-Feb-18 A	18-Jun-18	67											18-Jun-18, 066116 - Solid Surfacing Fabrications			
400	Rev and Appv - Solid Surfacing Fabrications	15	11	06-Feb-18 A	20-Apr-18	67											Rev and Appv - Solid Surfacing Fabrications			
410	Fab and Deliver - Solid Surfacing Fabrications	40	40	23-Apr-18	18-Jun-18	67											Fab and Deliver - Solid Surfacing Fabrications			
074646 - Mineral Fiber Cement Siding		27	60	20-Mar-18 A	29-Jun-18	9											29-Jun-18, 074646 - Mineral Fiber Cement Siding			
530	Fab and Deliver - Mineral Fiber Cement Siding	27	60	20-Mar-18 A	29-Jun-18	9											Fab and Deliver - Mineral Fiber Cement Siding			
076120 - Field-Formed Metal Roofing and Cladding		40	40	07-Mar-18 A	01-Jun-18	42											01-Jun-18, 076120 - Field-Formed Metal Roofing and Cladding			
610	Fab and Deliver - Field-Formed Metal Roofing and Cladding	40	40	07-Mar-18 A	01-Jun-18	42											Fab and Deliver - Field-Formed Metal Roofing and Cladding			
081113 - Hollow Metal Doors and Frames		40	5	30-Jan-18 A	12-Apr-18	135											12-Apr-18, 081113 - Hollow Metal Doors and Frames			
690	Fab and Deliver - Hollow Metal Doors and Frames	40	5	30-Jan-18 A	12-Apr-18	135											Fab and Deliver - Hollow Metal Doors and Frames			
084313 - Aluminum-Framed Storefronts		40	28	12-Jan-18 A	15-May-18	47											15-May-18, 084313 - Aluminum-Framed Storefronts			
730	Fab and Deliver - Aluminum-Framed Storefronts	40	28	12-Jan-18 A	15-May-18	47											Fab and Deliver - Aluminum-Framed Storefronts			
085113 - Aluminum Windows		40	28	24-Jan-18 A	15-May-18	34											15-May-18, 085113 - Aluminum Windows			
770	Fab and Deliver - Aluminum Windows	40	28	24-Jan-18 A	15-May-18	34											Fab and Deliver - Aluminum Windows			
086200 - Unit Skylights		40	18	17-Jan-18 A	01-May-18	57											01-May-18, 086200 - Unit Skylights			
810	Fab and Deliver - Unit Skylights	40	18	17-Jan-18 A	01-May-18	57											Fab and Deliver - Unit Skylights			
086300 - Metal-Framed Skylights		40	18	17-Jan-18 A	01-May-18	57											01-May-18, 086300 - Metal-Framed Skylights			
850	Fab and Deliver - Metal-Framed Skylights	40	18	17-Jan-18 A	01-May-18	57											Fab and Deliver - Metal-Framed Skylights			
096566 - Resilient Athletic Flooring		63	45	13-Mar-18 A	08-Jun-18	83											08-Jun-18, 096566 - Resilient Athletic Flooring			

project: DH06
data date: 06-Apr-18
run date: 27-Apr-18

Dedham Early Childhood

Schedule Update No.6 (as of 06-Apr-18)

**Early Childhood
Education Center**
Home to America's first tax supported, free public school


H.V. COLLINS
COMPANY

Activity ID	Activity Name	OD	RD	Early Start	Early Finish	TF	2018												2019	
							Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb			
323100 - Fencing							▼ 08-Jun-18, 323100 - Fencing													
1940	Bid & Award - Fencing	15	5	22-Sep-17 A	12-Apr-18	59	■ Bid & Award - Fencing													
1950	Prep & Fwd - Fencing	15	15	13-Apr-18	03-May-18	59	■ Prep & Fwd - Fencing													
1960	Rev and Appv - Fencing	15	15	04-May-18	24-May-18	59	■ Rev and Appv - Fencing													
1970	Fab and Deliver - Fencing	10	10	25-May-18	08-Jun-18	59	■ Fab and Deliver - Fencing													
329000 - Planting							▼ 14-Jun-18, 329000 - Planting													
1980	Bid & Award - Planting	15	9	22-Sep-17 A	18-Apr-18	60	■ Bid & Award - Planting													
1990	Prep & Fwd - Planting	5	5	19-Apr-18	25-Apr-18	60	■ Prep & Fwd - Planting													
2000	Rev and Appv - Planting	15	15	26-Apr-18	16-May-18	60	■ Rev and Appv - Planting													
2010	Fab and Deliver - Planting	20	20	17-May-18	14-Jun-18	60	■ Fab and Deliver - Planting													
PRECON							▼ 13-Apr-18, PRECON													
P100	Exterior Building Mockup	11	6	05-Jan-18 A	13-Apr-18	9	■ Exterior Building Mockup													
Construction							▼ 21-Dec-18, Constructi													
Site							▼ 26-Oct-18, Site													
6770	Excavate / Install / Backfill - UG Power	10	10	04-Jun-18	15-Jun-18	76	■ Excavate / Install / Backfill - UG Power													
6650	Excavate / Install / Backfill - UG Storm Drainage	10	10	04-Jun-18	15-Jun-18	32	■ Excavate / Install / Backfill - UG Storm Drainage													
6690	Site Lighting	5	5	06-Jun-18	12-Jun-18	32	■ Site Lighting													
6700	Curbing	15	15	13-Jun-18	03-Jul-18	32	■ Curbing													
6780	Form and Place Transformer Pad	3	3	18-Jun-18	20-Jun-18	76	■ Form and Place Transformer Pad													
6660	Excavate / Install / Backfill - Yard Drains	5	5	18-Jun-18	22-Jun-18	32	■ Excavate / Install / Backfill - Yard Drains													
6670	Final Grading	5	5	24-Jul-18	30-Jul-18	12	■ Final Grading													
6810	Excavate / Install / Backfill - Gas Service	5	5	31-Jul-18	06-Aug-18	39	■ Excavate / Install / Backfill - Gas Service													
6680	Construct Play Scapes	25	25	31-Jul-18	04-Sep-18	12	■ Construct Play Scapes													
6710	Sidewalks / Pads	30	30	07-Aug-18	18-Sep-18	9	■ Sidewalks / Pads													
6820	Form and Place Gas Equipement Pad	3	3	07-Aug-18	09-Aug-18	39	■ Form and Place Gas Equipement Pad													
6830	Set Gas Meter	2	2	10-Aug-18	13-Aug-18	39	■ Set Gas Meter													
6790	Set Transformer	1	1	14-Aug-18	14-Aug-18	39	■ Set Transformer													
6840	Final Gas Connections	5	5	14-Aug-18	20-Aug-18	48	■ Final Gas Connections													
6800	Pull Cables for Power	3	3	15-Aug-18	17-Aug-18	39	■ Pull Cables for Power													
6730	Fencing	30	30	16-Aug-18	27-Sep-18	12	■ Fencing													
6740	Bio Rention Landscaping	30	30	23-Aug-18	04-Oct-18	12	■ Bio Rention Landscaping													
6720	Fire Access Loop	15	15	19-Sep-18	09-Oct-18	9	■ Fire Access Loop													
6750	Final Paving	10	10	10-Oct-18	23-Oct-18	9	■ Final Paving													
6760	Traffic Markings	3	3	24-Oct-18	26-Oct-18	9	■ Traffic Markings													
Building							▼ 06-Nov-18, Building													
Foundation							▼ 18-May-18, Foundation													
3260	Backfill UG MEP / Prep SOG - Area A	4	26	27-Mar-18 A	11-May-18	7	■ Backfill UG MEP / Prep SOG - Area A													
3190	Prep and Place SOG - Area B	5	5	03-May-18*	09-May-18	5	■ Prep and Place SOG - Area B													
3270	Prep and Place SOG - Area A	5	5	14-May-18	18-May-18	7	■ Prep and Place SOG - Area A													
Structure							▼ 30-Apr-18, Structure													
3410	High Roof Decking - Area A	1	1	30-Apr-18*	30-Apr-18	0	■ High Roof Decking - Area A													
Enclosure							▼ 06-Aug-18, Enclosure													

Activity ID	Activity Name	OD	RD	Early Start	Early Finish	TF	2018												2019	
							Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb			
Area C		104	85	12-Mar-18 A	06-Aug-18	58	06-Aug-18, Area C													
3440	AVB/Roof Insulation/Sheathing	10	22	12-Mar-18 A	07-May-18	2	AVB/Roof Insulation/Sheathing													
3480	Air Vapor Barrier	7	21	27-Mar-18 A	04-May-18	9	Air Vapor Barrier													
3460	Asphalt Shingles	15	15	23-Apr-18*	11-May-18	63	Asphalt Shingles													
3510	Masonry	10	10	23-Apr-18*	04-May-18	48	Masonry													
3500	Windows	7	7	16-May-18	24-May-18	34	Windows													
3540	Set Roof Top Equipment & MEP Connections	20	20	18-Jun-18	16-Jul-18	73	Set Roof Top Equipment & MEP Connections													
3520	Trim/Siding	20	20	02-Jul-18	30-Jul-18	9	Trim/Siding													
3530	Gutters/Downspouts	5	5	31-Jul-18	06-Aug-18	9	Gutters/Downspouts													
Area B		60	60	01-May-18	25-Jul-18	66	25-Jul-18, Area B													
3570	Fascia Board	7	7	01-May-18*	09-May-18	0	Fascia Board													
3640	Air Vapor Barrier	3	3	07-May-18	09-May-18	9	Air Vapor Barrier													
3580	AVB/Roof Insulation/Sheathing	9	9	10-May-18	22-May-18	0	AVB/Roof Insulation/Sheathing													
3650	Windows	5	5	16-May-18	22-May-18	34	Windows													
3670	Masonry	5	5	23-May-18	30-May-18	34	Masonry													
3590	PVC Roofing	5	5	23-May-18	30-May-18	37	PVC Roofing													
3600	Set Skylight	5	5	31-May-18	06-Jun-18	37	Set Skylight													
3610	Standing Seam at Canopy	5	5	04-Jun-18	08-Jun-18	42	Standing Seam at Canopy													
7180	Set Roof Top Equipment & MEP Connections	20	20	18-Jun-18	16-Jul-18	73	Set Roof Top Equipment & MEP Connections													
3680	Trim/Siding	12	12	02-Jul-18	18-Jul-18	15	Trim/Siding													
3620	Gutter/Downspouts	5	5	19-Jul-18	25-Jul-18	17	Gutter/Downspouts													
Area A		53	59	05-Apr-18 A	16-Jul-18	73	16-Jul-18, Area A													
3740	Exterior Wall Framing/Sheathing/Blocking	6	6	05-Apr-18 A	30-Apr-18	25	Exterior Wall Framing/Sheathing/Blocking													
3750	Air Vapor Barrier	3	3	01-May-18	03-May-18	25	Air Vapor Barrier													
3690	Perimeter Roof Blocking	4	4	01-May-18	04-May-18	10	Perimeter Roof Blocking													
3760	Windows	5	5	04-May-18	10-May-18	32	Windows													
3700	Fascia Board	7	7	07-May-18	15-May-18	10	Fascia Board													
3780	Masonry	5	5	11-May-18	17-May-18	32	Masonry													
3710	AVB/Roof Insulation/Sheathing	7	7	16-May-18	24-May-18	10	AVB/Roof Insulation/Sheathing													
3790	Trim/Siding	12	12	18-May-18	05-Jun-18	32	Trim/Siding													
3720	Asphalt Shingles	5	5	25-May-18	01-Jun-18	32	Asphalt Shingles													
3730	Gutters/Downspouts	5	5	06-Jun-18	12-Jun-18	47	Gutters/Downspouts													
7190	Set Roof Top Equipment & MEP Connections	20	20	18-Jun-18	16-Jul-18	73	Set Roof Top Equipment & MEP Connections													
Interior		139	139	23-Apr-18	06-Nov-18	0	06-Nov-18, Interior													
Area C		139	139	23-Apr-18	06-Nov-18	0	06-Nov-18, Area C													
4000	HM Frame Interior Framing	5	5	23-Apr-18*	27-Apr-18	0	HM Frame Interior Framing													
4020	OH / Inwall Mechanical	20	20	23-Apr-18	18-May-18	10	OH / Inwall Mechanical													
4040	OH Ductwork / VAV Boxes	20	20	23-Apr-18	18-May-18	0	OH Ductwork / VAV Boxes													
4070	OH Sprinkler	15	15	23-Apr-18	11-May-18	25	OH Sprinkler													
4010	OH / Inwall Electrical	20	20	08-May-18	05-Jun-18	9	OH / Inwall Electrical													
4030	Mechanical Insulation	10	10	21-May-18	04-Jun-18	10	Mechanical Insulation													
4050	OH / Inwall Plumbing	15	15	21-May-18	11-Jun-18	0	OH / Inwall Plumbing													
4060	Plumbing Insulation	5	5	12-Jun-18	18-Jun-18	0	Plumbing Insulation													

Activity ID	Activity Name	OD	RD	Early Start	Early Finish	TF	2018												2019	
							Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb			
4080	MEP Inspection	2	2	19-Jun-18	20-Jun-18	0														
4090	Thermal Insulation	5	5	21-Jun-18	27-Jun-18	0														
4100	Insulation Inspection	2	2	28-Jun-18	29-Jun-18	0														
4110	Hang Drywall at Walls	15	15	02-Jul-18	23-Jul-18	0														
4120	Frame Soffits	15	15	10-Jul-18	30-Jul-18	0														
4130	Hang Drywall at Soffits / Ceilings	5	5	24-Jul-18	30-Jul-18	0														
4140	Tape and Sand Drywall	15	15	31-Jul-18	20-Aug-18	0														
4150	Prime Paint / 1st Coat	7	7	10-Aug-18	20-Aug-18	0														
4160	Ceiling Grid	15	15	17-Aug-18	07-Sep-18	0														
4170	HVAC Drops	5	5	31-Aug-18	07-Sep-18	0														
4180	Lighting Drops	5	5	31-Aug-18	07-Sep-18	0														
4190	Sprinkler Drops	5	5	31-Aug-18	07-Sep-18	0														
4200	Ceiling Tile	5	5	31-Aug-18	07-Sep-18	0														
4210	Epoxy Flooring	10	10	10-Sep-18	21-Sep-18	5														
4220	Resilent Flooring	15	15	10-Sep-18	28-Sep-18	0														
4230	Millwork / Casework	10	10	24-Sep-18	05-Oct-18	0														
4240	Plumbing Fixtures / Trim	10	10	01-Oct-18	12-Oct-18	7														
4250	Electrical Devices / Trim	10	10	03-Oct-18	16-Oct-18	0														
4260	Toilet Accessories	5	5	08-Oct-18	12-Oct-18	7														
4270	Final Paint	5	5	17-Oct-18	23-Oct-18	0														
4280	Doors / Hardware	5	5	24-Oct-18	30-Oct-18	0														
4290	MISC Specialties	5	5	31-Oct-18	06-Nov-18	0														
Area B		124	124	14-May-18	06-Nov-18	0														
6850	HM Frame Interior Framing	5	5	14-May-18	18-May-18	5														
6860	OH / Inwall Mechanical	10	10	14-May-18	25-May-18	10														
6910	OH Ductwork / VAV Boxes	20	20	14-May-18	11-Jun-18	10														
6940	OH / Inwall Plumbing	15	15	14-May-18	04-Jun-18	10														
6890	OH Sprinkler	15	15	14-May-18	04-Jun-18	15														
6880	OH / Inwall Electrical	20	20	29-May-18	25-Jun-18	0														
6900	Mechanical Insulation	10	10	29-May-18	11-Jun-18	10														
6980	Plumbing Insulation	5	5	05-Jun-18	11-Jun-18	10														
6920	MEP Inspection	2	2	26-Jun-18	27-Jun-18	0														
6930	Thermal Insulation	5	5	28-Jun-18	05-Jul-18	0														
6950	Insulation Inspection	2	2	06-Jul-18	09-Jul-18	0														
6960	Hang Drywall at Walls	15	15	10-Jul-18	30-Jul-18	0														
6970	Frame Soffits	15	15	17-Jul-18	06-Aug-18	0														
6990	Hang Drywall at Soffits / Ceilings	5	5	31-Jul-18	06-Aug-18	0														
7000	Tape and Sand Drywall	15	15	07-Aug-18	27-Aug-18	0														
7010	Prime Paint / 1st Coat	7	7	17-Aug-18	27-Aug-18	0														
7020	Ceiling Grid	15	15	21-Aug-18	11-Sep-18	0														
7030	HVAC Drops	5	5	05-Sep-18	11-Sep-18	0														
7040	Lighting Drops	5	5	05-Sep-18	11-Sep-18	0														
7050	Sprinkler Drops	5	5	05-Sep-18	11-Sep-18	0														

06-Nov-18, Area B

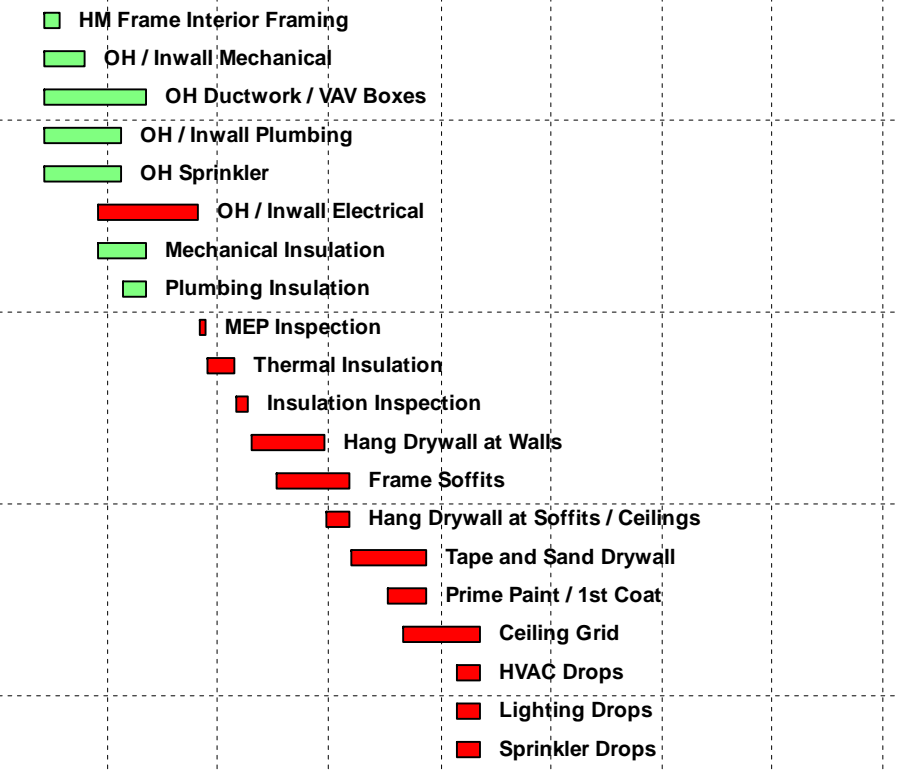

Activity ID	Activity Name	OD	RD	Early Start	Early Finish	TF	2018												2019	
							Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb			
7060	Ceiling Tile	5	5	05-Sep-18	11-Sep-18	0														
7070	Epoxy Flooring	10	10	12-Sep-18	25-Sep-18	0														
7080	Resilent Flooring	15	15	12-Sep-18	02-Oct-18	5														
7090	Millwork / Casework	10	10	26-Sep-18	09-Oct-18	0														
7100	Plumbing Fixtures / Trim	10	10	03-Oct-18	16-Oct-18	0														
6870	Electrical Devices / Trim	10	10	03-Oct-18	16-Oct-18	0														
7110	Toilet Accessories	5	5	17-Oct-18	23-Oct-18	0														
7120	Final Paint	5	5	17-Oct-18	23-Oct-18	0														
7130	Doors / Hardware	5	5	24-Oct-18	30-Oct-18	0														
7140	MISC Specialties	5	5	31-Oct-18	06-Nov-18	0														
Area A		109	109	23-May-18	25-Oct-18	8														
Overall		74	74	23-May-18	06-Sep-18	7														
6030	OH / Inwall Mechanical	15	15	23-May-18	13-Jun-18	12														
6000	HM Frame / Interior Framing	10	10	23-May-18	06-Jun-18	7														
6020	OH Ductwork / VAV Boxes	15	15	23-May-18	13-Jun-18	7														
6080	OH Sprinkler	10	10	23-May-18	06-Jun-18	27														
6090	Erect CMU Walls	15	15	23-May-18	13-Jun-18	10														
6010	OH / Inwall Electrical	15	15	25-May-18	15-Jun-18	10														
6050	OH / Inwall Plumbing	15	15	31-May-18	20-Jun-18	7														
6040	Mechanical Insulation	10	10	18-Jun-18	29-Jun-18	10														
6060	Plumbing Insulation	10	10	21-Jun-18	05-Jul-18	7														
6070	MEP Inspection	10	10	06-Jul-18	19-Jul-18	7														
6100	Thermal Insulation	5	5	20-Jul-18	26-Jul-18	7														
6110	Insulation Inspection	1	1	27-Jul-18	27-Jul-18	7														
6120	Hang Drywall at Walls	10	10	30-Jul-18	10-Aug-18	7														
6130	Frame Soffits	15	15	30-Jul-18	17-Aug-18	7														
6140	Hang Drywall at Soffits / Ceilings	5	5	13-Aug-18	17-Aug-18	7														
6150	Tape and Sand Drywall	10	10	20-Aug-18	31-Aug-18	7														
6160	Prime Paint / 1st Coat	8	8	27-Aug-18	06-Sep-18	7														
Kitchen		31	31	07-Sep-18	19-Oct-18	7														
6170	Ceramic Tile	10	10	07-Sep-18	20-Sep-18	7														
6180	Epoxy Flooring	5	5	21-Sep-18	27-Sep-18	7														
6190	OH Coiling Door	2	2	28-Sep-18	01-Oct-18	7														
6200	Kitchen Hood	3	3	28-Sep-18	02-Oct-18	7														
6210	Ceiling Grid	3	3	02-Oct-18	04-Oct-18	7														
6220	Lighting Drops	3	3	02-Oct-18	04-Oct-18	7														
6230	HVAC Drops	3	3	02-Oct-18	04-Oct-18	7														
6240	Sprinkler Drops	3	3	02-Oct-18	04-Oct-18	7														
6250	Ceiling Tile	3	3	05-Oct-18	09-Oct-18	7														
6260	Food Service Equipment	3	3	10-Oct-18	12-Oct-18	7														
6270	Food Service Equipment Connections	5	5	15-Oct-18	19-Oct-18	7														
Electrical Room		30	30	13-Aug-18	24-Sep-18	19														
6300	Set Switchgear	3	3	13-Aug-18	15-Aug-18	19														

- Ceiling Tile
- Epoxy Flooring
- Resilent Flooring
- Millwork / Casework
- Plumbing Fixtures / Trim
- Electrical Devices / Trim
- Toilet Accessories
- Final Paint
- Doors / Hardware
- MISC Specialties

25-Oct-18, Area A

06-Sep-18, Overall

- OH / Inwall Mechanical
- HM Frame / Interior Framing
- OH Ductwork / VAV Boxes
- OH Sprinkler
- Erect CMU Walls
- OH / Inwall Electrical
- OH / Inwall Plumbing
- Mechanical Insulation
- Plumbing Insulation
- MEP Inspection
- Thermal Insulation
- Insulation Inspection
- Hang Drywall at Walls
- Frame Soffits
- Hang Drywall at Soffits / Ceilings
- Tape and Sand Drywall
- Prime Paint / 1st Coat
- Ceramic Tile
- Epoxy Flooring
- OH Coiling Door
- Kitchen Hood
- Ceiling Grid
- Lighting Drops
- HVAC Drops
- Sprinkler Drops
- Ceiling Tile
- Food Service Equipment
- Food Service Equipment Connections
- Set Switchgear

19-Oct-18, Kitchen

24-Sep-18, Electrical Room

Activity ID	Activity Name	OD	RD	Early Start	Early Finish	TF	2018												2019	
							Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb			
6310	Panels	2	2	16-Aug-18	17-Aug-18	19														
6320	Electrical Rough	15	15	20-Aug-18	10-Sep-18	19														
6330	Cabling	6	6	04-Sep-18	11-Sep-18	19														
6340	Terminations	5	5	11-Sep-18	17-Sep-18	19														
6350	Energize Electrical Service	5	5	18-Sep-18	24-Sep-18	19														
Gym		35	35	07-Sep-18	25-Oct-18	8														
6380	Paint Overhead Surfaces	6	6	07-Sep-18	14-Sep-18	8														
6390	Lighting Drops	5	5	17-Sep-18	21-Sep-18	8														
6400	HVAC Drops	5	5	17-Sep-18	21-Sep-18	8														
6410	Gym Equipment	2	2	24-Sep-18	25-Sep-18	8														
6420	Rubber Flooring	10	10	26-Sep-18	09-Oct-18	8														
6430	Operable Partition	3	3	10-Oct-18	12-Oct-18	8														
6440	Pads	3	3	15-Oct-18	17-Oct-18	8														
6450	MISC Specialties	6	6	18-Oct-18	25-Oct-18	8														
General Areas		38	38	29-Aug-18	22-Oct-18	11														
6500	Ceiling Grid	10	10	29-Aug-18	12-Sep-18	11														
6510	HVAC Drops	10	10	30-Aug-18	13-Sep-18	11														
6520	Lighting Drops	10	10	30-Aug-18	13-Sep-18	11														
6530	Sprinkler Drops	10	10	30-Aug-18	13-Sep-18	11														
6540	Ceiling Tile	5	5	07-Sep-18	13-Sep-18	11														
6550	Ceramic Tile	10	10	14-Sep-18	27-Sep-18	11														
6560	Epoxy Flooring	10	10	14-Sep-18	27-Sep-18	14														
6570	Resilient Flooring	15	15	14-Sep-18	04-Oct-18	11														
6580	Millwork/ Casework	2	2	03-Oct-18	04-Oct-18	11														
6590	Plumbing Fixtures Trim	10	10	05-Oct-18	18-Oct-18	12														
6600	Electrical Devices / Trim	10	10	05-Oct-18	18-Oct-18	11														
6620	Final Paint	5	5	15-Oct-18	19-Oct-18	11														
6630	Doors	5	5	15-Oct-18	19-Oct-18	11														
6610	Toilet Accessories	3	3	16-Oct-18	18-Oct-18	12														
6640	MISC Specialties	5	5	16-Oct-18	22-Oct-18	11														
Closeout		63	63	25-Sep-18	21-Dec-18	0														
6360	Startup / Checkout Electrical Service	5	5	25-Sep-18	01-Oct-18	19														
6460	HVAC- Startup/ Checkout	7	7	02-Oct-18	10-Oct-18	19														
6280	Startup / Checkout - Food Service Equipment	2	2	22-Oct-18	23-Oct-18	7														
6290	Dept. of Health Inspection	5	5	24-Oct-18	30-Oct-18	7														
7150	HVAC Test & Balance / Commissioning	7	7	31-Oct-18	08-Nov-18	0														
6490	Final Inspection	6	6	09-Nov-18	16-Nov-18	0														
7160	Obtain Certificate of Occpancy (GOAL 9/21/18)	2	2	19-Nov-18	20-Nov-18	0														
7170	Punch List	22	22	21-Nov-18	21-Dec-18	0														

